

Homework: Schedule Management Report IT Project Management

Exercises 1

Student Name: Trần Anh Tuấn


Student ID: 24521943

Course ID: MSIS3033.Q21.CTTT


April 1, 2026

1 Draw the Network Diagrams in AOA and AON format

1.1 Activity on Arrow (AOA)

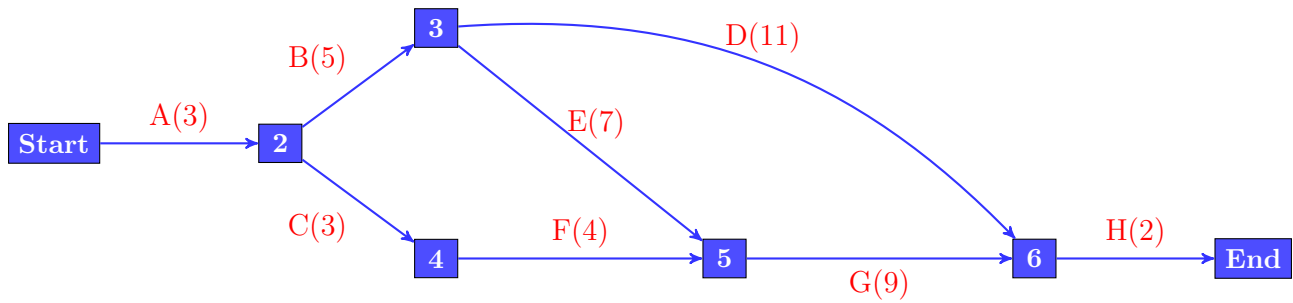

1.2 Activity on Node (AON)

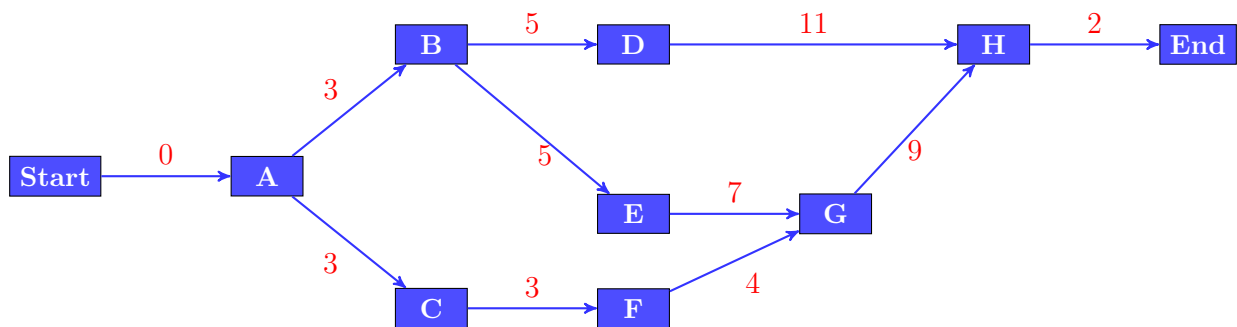

2 Find the Critical Paths

Analyze the lengths of the paths:

- **Path 1:** $A \rightarrow B \rightarrow D \rightarrow H = 3 + 5 + 11 + 2 = 21$
- **Path 2:** $A \rightarrow B \rightarrow E \rightarrow G \rightarrow H = 3 + 5 + 7 + 9 + 2 = 26$
- **Path 3:** $A \rightarrow C \rightarrow F \rightarrow G \rightarrow H = 3 + 3 + 4 + 9 + 2 = 21$

Result:

- **Critical Path:** $A - B - E - G - H$
- **Total duration:** 26

3 Calculate the Earliest Start and Latest Start time of each task

Task	t (Earliest Start Time)	T (Latest Start Time)
*A	0	0
*B	3	3
C	3	8
D	8	13
*E	8	8
F	6	11
*G	15	15
*H	24	24

4 Calculate the Total Float and Free Float of each task.

- **Total Float (M_i):** $M_i = T_i - t_i$
- **Free Float (m_i):** $m_i = t_j - t_i - t_{ij}$

Task	Total Float (M_i)	Free Float (m_i)
*A	0	0
*B	0	0
C	5	0
D	5	5
*E	0	0
F	5	5
*G	0	0
*H	0	0
